

LAB 3: PROJECT SCHEDULE

- **Purpose:** Make a schedule for your project
- **Submission:**
 - Work Breakdown Structure
 - Product Backlog and Sprint Backlog

1. Work Breakdown Structure

After collecting requirements and defining the scope, the next step is creating a work breakdown structure (WBS).


There are two standard methods of creating WBSs: top-down and bottom-up approaches.

- Top-down approach: starting with the most significant items of the project and break them into subordinate items.
- Bottom-up approach: First, identify as many specific tasks related to the project as possible, then aggregate the particular tasks and organize them into summary activities or higher levels in the WBS.


Example: An example of using top-down approach to create a WBS

Project Name: ONLINE BOOKSTORE SYSTEM

Following the Software Development Life Cycle, the process includes: Requirement Analysis, Design, Implementation, Testing, Deployment and Maintenance.



Then, in each phase, you break it into smaller tasks. For example, in the Analysis phase, you can break into 3 activities, which are Gathering business requirements, creating process diagrams, and performing a detailed analysis.

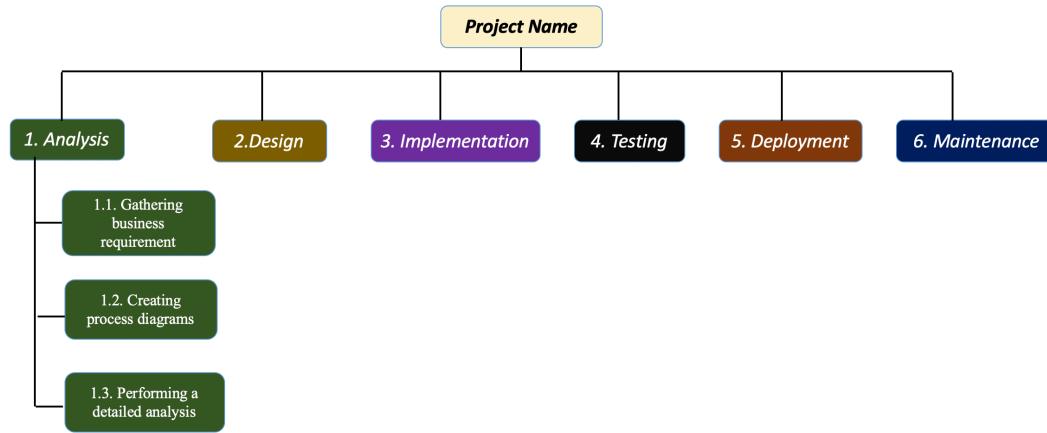

Then, continue breaking them into smaller ones.

2. Product Backlog and Sprint Backlog

- The product backlog lists all the tasks and specifications required to complete the final product.
- The sprint backlog is smaller in scope and less dynamic than the product backlog. When items are moved from the product backlog to the sprint backlog, they are broken down into more detailed tasks.

Example:

- **Product Backlog**
 - **Story name and description** – This is a brief identifying description of the task to be performed by the backlog item.
 - **Status:** the status of backlog item. It can be Open (initial status), In progress and Complete
 - **Sprint :** The sprint ID that this story belong to
 - **Priority:** The priority of the backlog item. Values for priority are Low, Medium, and High.
 - **Estimated days:** estimated duration to finish the task.
 - **Comments:** You can add comments here to add key detail or explanation to the story. For larger definitions, use external tools and materials.

StoryID	Story Name and description	Status	Sprint	Piority	Estimated days	Comments
001	As a member, I want to login to the site, so that I can do online shopping	Open	1	High	7 days	
...		...	...	...	...	...

▪ ***Sprint Backlog***

- ***Tasks:*** define all tasks belong to the sprint.
- ***Responsibilties:*** members in charge

Sprint ID: Sprint Name (ex: Sprint1- System login)						
Tasks	Responsibilites	Monday	Tuesday	Wednesday	Thursday	Friday
Define the use case and requirements for the login function	Team	x hour(s)			...	...
Design login function	Designer	...	...	...	...	...
...	...			...	...	...
